BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Improvements to roads,drains and other development works at Yelahanka old town, Maruthinagara, sapthagiri layout Gandhinagara KHB Colony, Nehru nagara, Shivanahalli, PDMS APTS Premies and Surrounding areas in Ward No 01 of Yelahanka Division under Amruth Nagarothana Grants(PACKAGE NO 01)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-03-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Schedule -B Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of	Cum	12.04	12.04	100	03-09-22	01-02-23	151
2	Earth work excavation by manual means for drains,canals, waste weir, draft, approach channels, key trenches, foundation of bridges and such simillar works in all kinds of soils , as per drawing and technical specifications, including setting out, shoring, strutting,	Cum	3645.06	3645.06	100	05-09-22	19-12-22	105
3	Providing and laying in position plain cement concrete for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150	Cum	588.71	588.71	100	20-09-22	25-12-22	96
4	Providing and laying in position Reinforced cement concrete for all Super structures of building , Road works, Water works, Irrigation works & super structure works of bridges upto 3.50 m height. The granite/ trap/basalt crushed graded coarse aggregates	Cum	9.58	9.58	100	05-09-22	25-02-23	173
5	Supplying, Fitting and Placing un-coated TMT bar Reinforcement in sub-structure complete as per Drawing and Technical Specifications.	Tonne	63.74	63.74	100	25-09-22	20-12-22	86
6	Providing and laying flamed finish Granite stone flooring in required design and patterns, in linear as well as curvilinear portions of the building all complete as per the architectural drawings with 18 mm thick stone slab over 20 mm (average) thick	Sqm	28.8	28.8	100	05-09-22	25-02-23	173
7	Providing and laying flooring and steps machine cut granite slabs 40 mm thick on cement mortar bed 1:6, 25 mm thick, and pointed with cement mortar 1:3 over existing cement concrete bed , including cost of materials, mortar labour, curing complete as per	Sqm	22.62	22.62	100	10-09-22	25-09-22	15

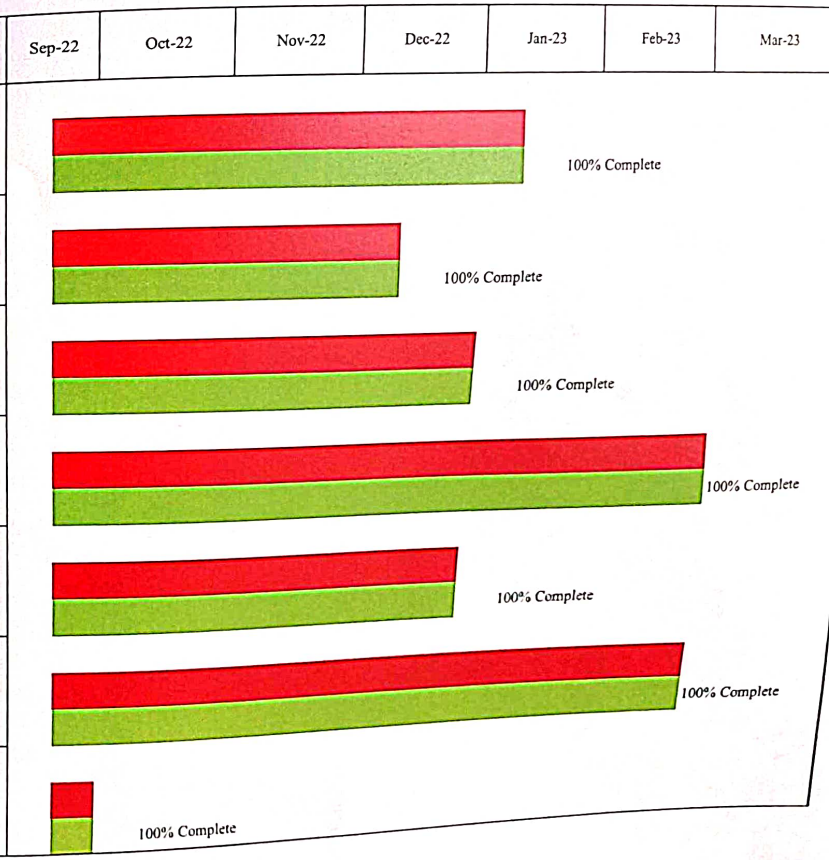

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP Ynk. Zn)

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Improvements to roads,drains and other development works at Yelahanka old town, Maruthinagara, sapthagiri layout Gandhinagara KHB Colony, Nehru nagara, Shivanahalli, PDMS APTS Premies and Surrounding areas in Ward No 01 of Yelahanka Division under Amruth Nagarothana Grants(PACKAGE NO 01)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-03-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Schedule -B Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
8	Providing Size Stone masonry with hard stone in foundation & plinth with Cement mortar 1:6 (1 cement : 6 coarse sand)	Cum	231.09	231.09	100	10-09-22	10-10-22	30
9	Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers, laid in layers, well compacted using	Cum	17.8	17.80	100	30-09-22	20-12-22	81
10	Ruled/ Flush pointing on White sand stone masonry surface with lime, surkhi and marble dust mortar in the ratio of 1:1.5:1/2 {One lime : 1.5 surkhi (15% dark red and 85% light yellow surkhi) : 1/2 marble dust}. (The rate is inclusive of all aterials & labours involved except scaffolding).	Sqm	134.86	134.86	0	05-09-22	10-10-22	35
11	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x200x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM	Sqm	440.35	440.35	100	30-09-22	20-12-22	81
12	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x100x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM	Sqm	0	0	0	05-09-22	25-02-23	173
13	Providing 12 mm cement plaster finished with a floating coat of neat cement of mix :1:3 (1 cement: 3 fine sand) to brick masonry including rounding off corners wherever required smooth rendering, providing and removing scaffolding, including cost of	Sqm	72.98	72.98	100	05-09-22	25-02-23	173
14	Providing 18 mm cement plaster in two coats under layer 12 mm thick cement plaster with cement mortar 1:5 (1 cement : 5 coarse sand) and a top layer 6 mm thick cement plaster with cement mortar 1:3 (1 cement : 3 coarse sand) finished rough with sponge to brick masonry including rounding off corners wherever required smooth rendering, providing and removing scaffolding, including	Sqm	655.27	655.27	100	05-09-22	20-01-23	137

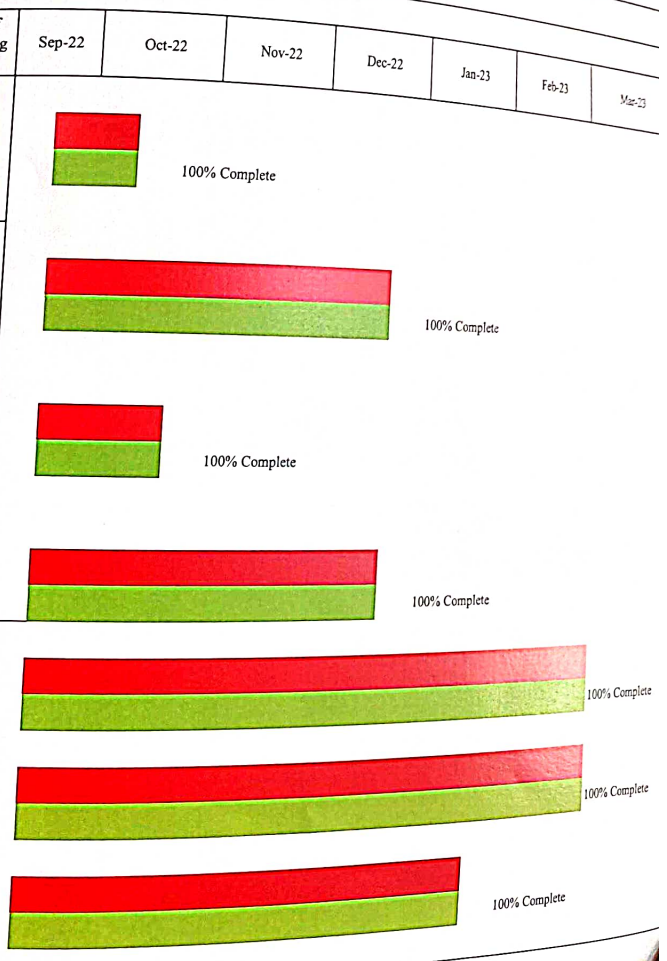

Asst. Executive Engineer
Yelahanka Sub. Division

BRUHAT BENGALURU MAHANAGARA PALIKE

lients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Improvements to roads,drains and other development works at Yelahanka old town, Maruthinagara, sapthagiri layout Gandhinagara KHB Colony, Nehru nagara, Shivanahalli, PDMS APTS Premies and Surrounding areas in Ward No 01 of Yelahanka Division under Amruth Nagarothana Grants(PACKAGE NO 01)
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	03-09-22
Project End Date	:	03-03-23
Project Length in Months	:	6 Months

Sl. No	Assignment	Unit	Schedule -B Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
64	Supply and fixing of Retro Reflective Single Arrow Road Name Signboard of size 1600mm x 900mm made out of retro reflective sheeting conforming to Type XI standards of ASTM D 4956-09 & as per IRC 67-2012 for full back ground of blue colour & white letters and fixed over 4 mm thick Aluminium Composite Material sheet having minimum 0.5 mm thick Aluminium skin on both	Nos	87	87	100	05-09-22	25-02-23	173
65	Supplying and Fixing of Molded Shank Raised Pavement Markers / Cat's Eye made of polycarbonate and ABS moulded body and reflective panels with micro prismatic lens capable of providing total internal reflection of the light entering the lens face and shall	Nos	609	609	100	05-09-22	25-02-23	173
66	Lead for Disposal of Debris	Cum	7698.89	7698.89	92	05-09-22	05-01-23	122

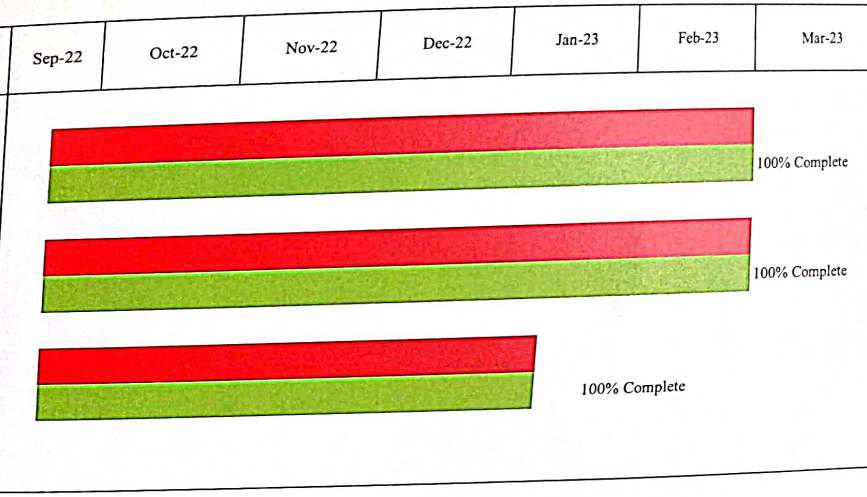

= Planned %

= Executed %

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP Ynk. Zn)
Yelahanka, Bangalore

RUDRAPRASAD CONSULTANTS
BANGALORE
